MONTANA CONTRACTING

Status: Active Estimates
Contact:
Date: 01/10/2025

Estimate: 24100 Camp Ramaquois Pavilion

Estimate Unit Costs

Line	Description	Quantity	Unit Cost	Total
1	**01 General Requirements**			
2	**01.0050 General Requirements**			
3	General Supervision (Per Week)	1.20 WK	3,461.54	4,153.85
4	Supervision (Per Week)	12.00 WK	2,400.00	28,800.00
5	General Labor (Per Week)	1.00 WK	1,400.00	1,400.00
6	Senior Project Manager (Per Week) [Projects > $3m]	4.00 WK	3,486.00	13,944.00
7	Blueprints (Per Page)	100.00 EA	6.00	600.00
8	Assistant Project Manager (Per Week)	1.00 WK	2,000.00	2,000.00
9	Misc. Materials (.005% Revenue)	1.00 LS	1,500.00	1,500.00
10	Temporary Toilet(s) (Per Month)	6.00 MO	185.00	1,110.00
11			**General Requirements Total**	**$53,507.85**
12			**General Requirements Total**	**$53,507.85**
13	**02 Existing Conditions**			
14	**02.1500 Containers/Waste Removal**			
15	Containers/Waste Removal	1.00 LS	1,500.00	1,500.00
16			**Containers/Waste Removal Total**	**$1,500.00**
17			**Existing Conditions Total**	**$1,500.00**
18	**03 Concrete**			
19	**03.1000 Concrete**			
20	Form & Pour 18"x48" Piers w/6" Base Pads @ 20' Intervals	77.00 EA	375.00	28,875.00
21	Form & Pour 12"x18" Grade Beams	39.71 CY	575.00	22,833.25
22			**Concrete Total**	**$51,708.25**
23			**Concrete Total**	**$51,708.25**
24	**13 Special Construction**			
25	**13.3400 Fabricated Engineered Structures**			
26	20' High Pre-Fabricated Metal Building + Engineering	24,600.00 SF	22.02	541,692.00
27			**Fabricated Engineered Structures Total**	**$541,692.00**
28			**Special Construction Total**	**$541,692.00**
29	**26 Electrical**			
30	**26.0000 Electric**			
31	I/O 24' Diameter Big Ass Fan(s) (Powerfoil X3.0)	3.00 EA	1,750.00	5,250.00
32	Duplex Receptacle	33.00 EA	175.00	5,775.00
33	Install Lighting Fixture	25.00 EA	200.00	5,000.00
34	Single-Pole Switch (Commercial)	9.00 EA	175.00	1,575.00
35	Temporary Lighting (SF)	24,600.00 SF	0.25	6,150.00
36	200 Amp Service	1.00 LS	6,000.00	6,000.00
37	Primary Service Up Pole	1.00 LS	900.00	900.00
38	Primary Service	130.60 LF	22.00	2,873.20
39			**Electric Total**	**$33,523.20**
40	**26.5000 Lighting Fixtures & Fans**			
41	Lighting Fixture Budget	25.00 EA	200.00	5,000.00

Line	Description	Quantity	Unit Cost	Total
42	F/O 24' Diameter Big Ass Fan(s) (Powerfoil X3.0)	3.00 EA	5,000.00	15,000.00
43			**Lighting Fixtures & Fans Total**	**$20,000.00**
44			**Electrical Total**	**$53,523.20**
45	**31 Sitework**			
46	**31.0000 Sitework**			
47	Pull Stumps in Area of Site Work & Haul Off Site	1.00 LS	4,200.00	4,200.00
48	Misc. Site Related Work (Fence Modifications, Staging, etc.)	1.00 LS	5,000.00	5,000.00
49	Excavate & Backfill Piers & Grade Beams	77.00 EA	100.00	7,700.00
50	Backfill/Compact Piers	77.00 EA	165.00	12,705.00
51	Prepare Slab Subgrade and Compact	24,600.00 SF	1.05	25,830.00
52	Trenching, Sand and Backfill Utility Trench for Underground Electric (2' Deep w/1' Sand)	130.60 LF	21.25	2,775.25
53			**Sitework Total**	**$58,210.25**
54	**31.1050 Fill Export**			
55	Export Fill (Hard Entry)	984.60 CY	34.00	33,476.40
56			**Fill Export Total**	**$33,476.40**
57	**31.1100 Drainage & Stormwater**			
58	Drainage & Stormwater	1.00 LS	103,000.00	103,000.00
59			**Drainage & Stormwater Total**	**$103,000.00**
60	**31.2500 Erosion And Sedimentation Controls**			
61	F/I Silt Fence	916.28 LF	4.00	3,665.12
62	F/I Construction Entrance	1.00 EA	2,900.00	2,900.00
63			**Erosion And Sedimentation Controls Total**	**$6,565.12**
64			**Sitework Total**	**$201,251.77**
65	**32 Exterior Improvements**			
66	**32.3200 Retaining Wall**			
67	F/I Retaining Wall	380.10 SF	60.00	22,806.00
68			**Retaining Wall Total**	**$22,806.00**
69			**Exterior Improvements Total**	**$22,806.00**
70	**Sub-Total (Base Cost)**			**$925,989.07**

Estimate Summary

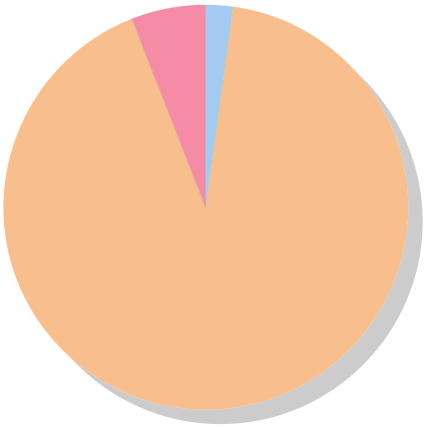

Material [$20,000]
Labor [$0]
SubContractor [$850,981]
Equipment [$0]
Other [$55,008]

Description		Total
Sub-Total (Base Cost)		$925,989.07
Sub-Total ()		$925,989.07
Overhead & Profit	15.0000%	138,898.36
Insurance	3.0000%	31,946.62
Total Estimate		$1,096,834.05
