Status: Active Estimates
Contact:
Date: 06/25/2025

Estimate: 250107 Haverstraw Elks

Estimate Unit Costs

Line	Description	Quantity	Unit Cost	Total
1	**01 General Requirements**			
2	**01.0050 General Requirements**			
3	Supervision (Per Week)	4.00 WK	2,400.00	9,600.00
4	General Labor (Per Week)	1.00 WK	1,400.00	1,400.00
5	Blueprints (Per Page)	40.00 EA	6.00	240.00
6	Misc. Materials (.005% Revenue)	1.00 LS	2,000.00	2,000.00
7	Temporary Toilet(s) (Per Month)	1.00 MO	225.00	225.00
8	Project Manager I (Per Week)	1.00 WK	2,400.00	2,400.00
9			**General Requirements Total**	**$15,865.00**
10			**General Requirements Total**	**$15,865.00**
11	**02 Existing Conditions**			
12	**02.1500 Containers/Waste Removal**			
13	30-Yard Container	1.00 EA	925.00	925.00
14	20-Yard Masonry Container	2.00 EA	950.00	1,900.00
15			**Containers/Waste Removal Total**	**$2,825.00**
16			**Existing Conditions Total**	**$2,825.00**
17	**03 Concrete**			
18	**03.1000 Concrete**			
19	Dowel New Foundation Into Existing Foundation With (2) #4 Rebars Spaced @ 16" O.C. Vertically Anchored With Hydraulic Cement	3.00 EA	250.00	750.00
20	Form & Pour Concrete Footings	10.29 CY	625.00	6,431.25
21	Form & Pour Concrete Foundation Wall(s)	32.39 CY	625.00	20,243.75
22	Form & Pour Concrete Slab. F/I All Applicable Rebar, Vapor Barrier & Mesh.	6.63 CY	585.00	3,878.55
23	Form & Pour Sonotube Footings	1.27 CY	850.00	1,079.50
24	Form & Pour Exterior Concrete Stairs (Per Risers). F/I All Applicable Rebar Per Plans & Specifications.	8.00 EA	1,250.00	10,000.00
25			**Concrete Total**	**$42,383.05**
26			**Concrete Total**	**$42,383.05**
27	**04 Masonry**			
28	**04.1000 Masonry**			
29	F/I CMU Split-Face Block [12"x8"x16"]	298.64 BLOCK	32.00	9,554.99
30	F/I CMU Split-Face Block [12"x8"x16"]	64.00 BLOCK	32.00	2,047.68
31			**Masonry Total**	**$11,602.67**
32	**04.4300 Stone Masonry**			
33	F/I Owens Corning Cultured Stone Veneer [Style & Color By Owner]	262.51 SF	65.00	17,063.15
34			**Stone Masonry Total**	**$17,063.15**
35			**Masonry Total**	**$28,665.82**
36	**05 Metal**			
37	**05.0100 Misc. Steel**			
38	F/I 1-1/2" Pipe Guardrail	36.17 LF	150.00	5,425.50
39	F/I 1-1/2" Pipe Guardrail	141.93 LF	150.00	21,289.50

Line	Description	Quantity	Unit Cost	Total
40	F/I 1-1/2" Pipe Handrail	12.64 LF	75.00	948.00
41			**Misc. Steel Total**	**$27,663.00**
42	**05.7610 Angle Irons**			
43	F/I Lintels	4.19 LF	175.00	733.25
44			**Angle Irons Total**	**$733.25**
45			**Metal Total**	**$28,396.25**
46	**06 Wood , Plastic and Composites**			
47	**06.4001 Wood Framing Materials**			
48	F/O 2x8 PT	66.00 LF	3.14	207.50
49	F/O 2x10 DF	652.63 LF	4.10	2,678.39
50	F/O 2x10x12' PT	66.00 LF	4.24	280.00
51	F/O 6"x6"x16' PT Post	6.00 EA	250.00	1,500.00
52	F/O 1-3/4" x 11-7/8" LVL	226.10 LF	8.66	1,958.93
53	F/O 4x8x5/8" CDX Fir Plywood	870.17 SF	2.02	1,761.90
54	F/O Simpson ABU66Z Post Base	6.00 EA	50.00	300.00
55			**Wood Framing Materials Total**	**$8,686.73**
56	**06.4002 Wood Framing Labor**			
57	I/O Roof Framing & Sheathing	870.17 SF	7.00	6,091.19
58	I/O Deck Post	6.00 EA	45.00	270.00
59			**Wood Framing Labor Total**	**$6,361.19**
60			**Wood , Plastic and Composites Total**	**$15,047.92**
61	**07 Thermal and Moisture Protection**			
62	**07.1000 Waterproofing**			
63	F/I Bituminous Dam Proofing	383.73 SF	4.50	1,726.79
64			**Waterproofing Total**	**$1,726.79**
65	**07.3000 Roofing**			
66	F/I Solid Vinyl Soffit	758.19 SF	6.00	4,549.14
67	F/I Fascia Board Wrapped In Aluminum To Match Existing	108.48 LF	20.00	2,169.60
68	F/I EPDM Roof	957.19 SF	18.00	17,229.42
69			**Roofing Total**	**$23,948.16**
70			**Thermal and Moisture Protection Total**	**$25,674.95**
71	**08 Openings**			
72	**08.1100 HM Doors, Frames & HW**			
73	F/O HM Frame (Single)	1.00 EA	375.00	375.00
74	F/O HM Door	1.00 EA	400.00	400.00
75	F/O Door Hardware (Commercial Exterior)	1.00 EA	1,075.00	1,075.00
76			**HM Doors, Frames & HW Total**	**$1,850.00**
77			**Openings Total**	**$1,850.00**
78	**09 Finishes**			
79	**09.2300 Carpentry**			
80	I/O Exterior HM Door, Frame & HW (Single)	1.00 EA	350.00	350.00

Line	Description	Quantity	Unit Cost	Total
81			**Carpentry Total**	**$350.00**
82	**09.9100 Painting**			
83	Paint HM Door & Frame (Single)	1.00 EA	200.00	200.00
84			**Painting Total**	**$200.00**
85			**Finishes Total**	**$550.00**
86	**26 Electrical**			
87	**26.0000 Electric**			
88	Inspection, Misc. Feeds, Etc.	1.00 LS	1,595.00	1,595.00
89	I/O Lighting Fixture	22.00 EA	185.00	4,070.00
90	I/O Lighting Fixture	3.00 EA	185.00	555.00
91	F/I Single-Pole Switch	2.00 EA	140.00	280.00
92			**Electric Total**	**$6,500.00**
93	**26.5000 Lighting Fixtures (Budget)**			
94	F/O Lighting Fixture(s) ($150/Allowance)	25.00 EA	150.00	3,750.00
95			**Lighting Fixtures (Budget) Total**	**$3,750.00**
96			**Electrical Total**	**$10,250.00**
97	**28 Safety And Security**			
98	**28.4600 Fire Alarm**			
99	Relocate Fire Alarm Box	1.00 EA	1,200.00	1,200.00
100			**Fire Alarm Total**	**$1,200.00**
101			**Safety And Security Total**	**$1,200.00**
102	**31 Sitework**			
103	**31.0000 Earthwork**			
104	Relocate Existing Monument Stone	1.00 EA	600.00	600.00
105	Remove Existing Plant Bed	92.22 SF	3.00	276.66
106	Excavate Foundation (Slab on Grade)	0.22 DAY	2,600.00	572.00
107	Excavate Foundation (Frost Walls)	1.38 DAY	2,600.00	3,588.00
108	Backfill Frost Walls	1.26 DAY	2,600.00	3,276.00
109	Backfill Slab & Compact	0.27 DAY	2,600.00	702.00
110	F/I Crushed Stone	80.40 CY	110.00	8,844.00
111			**Earthwork Total**	**$17,858.66**
112	**31.0050 Site Demolition**			
113	Remove Concrete Slab	67.82 SF	12.00	813.84
114	Remove Existing Concrete Landing	92.51 SF	10.00	925.10
115	Remove Existing Concrete Stairs	6.00 EA	150.00	900.00
116	Remove and Dispose of Existing Asphalt	420.39 SF	5.25	2,207.05
117			**Site Demolition Total**	**$4,845.99**
118			**Sitework Total**	**$22,704.65**
119	**32 Exterior Improvements**			
120	**32.1200 Paving**			
121	Patch Asphalt	50.20 SF	25.00	1,255.00

Line	Description	Quantity	Unit Cost	Total
122			**Paving Total**	**$1,255.00**
123	**32.1600 Site Concrete**			
124	F/I 4" Sidewalk w/6"Aggregate Base	145.36 SF	12.00	1,744.32
125			**Site Concrete Total**	**$1,744.32**
126			**Exterior Improvements Total**	**$2,999.32**
127	**Sub-Total (Base Cost)**			**$198,411.95**

Estimate Summary

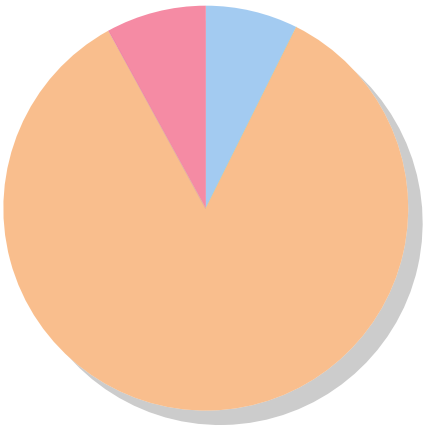

Material [$14,611]
Labor [$0]
SubContractor [$167,936]
Equipment [$0]
Other [$15,865]

Description		Total
Sub-Total (Base Cost)		$198,411.95
Material	10.0000%	1,461.08
SubContractor	9.0000%	15,114.26
Sub-Total (Direct Cost)		$214,987.28
Overhead & Profit	20.0000%	42,997.46
Total Estimate		$257,984.74
