LEGACY BUILDERS

Status: Active Estimates
Contact:
Date: 01/17/2025

Estimate: 250001 829 Milano Boutique

Estimate Unit Costs

Line	Description	Quantity	Unit Cost	Total
1	**01 General Requirements**			
2	**01.0050 General Requirements**			
3	Senior Superintendent	78.00 WK	4,000.00	312,000.00
4	General Labor	100.00 WK	1,200.00	120,000.00
5	Senior Project Manager	50.00 WK	4,000.00	200,000.00
6	Blueprints (Per Page)	2,500.00 EA	6.00	15,000.00
7	Construction Office (Equipment)	1.00 EA	3,600.00	3,600.00
8	Assistant Project Manager	78.00 WK	2,400.00	187,200.00
9	Misc. Materials	1.00 LS	50,000.00	50,000.00
10	Temporary Toilet(s) (Per Month)	36.00 MO	175.00	6,300.00
11	Material Hoist	10.00 MO	5,000.00	50,000.00
12	Cameras	20.00 MO	700.00	14,000.00
13	Construction Signage	1.00 LS	2,500.00	2,500.00
14	Procore Cost Allocation (.2%)	1.00 LS	23,500.00	23,500.00
15	Tele Handler/Forklift Rental	10.00 MO	3,500.00	35,000.00
16			**General Requirements Total**	**$1,019,100.00**
17	**01.5426 Mast Climbers**			
18	Mast Climber Rental	18.00 MO	10,000.00	180,000.00
19	Mast Climber Delivery, Setup & Removal	3.00 EA	11,000.00	33,000.00
20	Mast Climber Anchors and Bracing	3.00 EA	7,500.00	22,500.00
21			**Mast Climbers Total**	**$235,500.00**
22	**01.5600 Temporary Barriers And Enclosures**			
23	6' Chainlink Temporary Panel Fencing w/Privacy Mesh (18 Month Rental)	299.06 LF	50.00	14,953.00
24	F/I Temporary Guardrails, Posts, Base Plates and Toe Boards (Includes Removal)	980.00 LF	20.00	19,600.00
25	F/I Safety Nets	11,760.00 SF	2.75	32,340.00
26			**Temporary Barriers And Enclosures Total**	**$66,893.00**
27			**General Requirements Total**	**$1,321,493.00**
28	**02 Existing Conditions**			
29	**02.1000 Demolition**			
30	Remove Interior CMU Walls (Machine)	9.22 LF	35.00	322.70
31	Remove Roof Framing & Shingles (By Machine)	2,608.12 SF	1.50	3,912.18
32	Remove Building Envelope (Foundation, Flooring, CMU Walls, Exterior Doors, Windows & Roof) (By Machine)	1,575.00 SF	12.00	18,900.00
33	Exterior Utility Disconnects Prior to Demolition	1.00 LS	2,600.00	2,600.00
34	Surgically Cut Wall & Roof Away from Portion of House Being Salvaged (By Hand)	24.00 LF	50.00	1,200.00
35	Sawcut Existing Slab Where Portion of House is Being Salvaged	24.00 LF	35.00	840.00
36	Remove Pavers (By Machine)	376.42 SF	5.00	1,882.10
37	Remove Concrete Steps, Landings & Railings (By Machine)	253.58 SF	15.15	3,841.74
38	Remove Plantings @ Perimeter of Yard	113.02 LF	20.00	2,260.40
39	Remove Sidewalks	159.84 SF	12.00	1,918.08

Line	Description	Quantity	Unit Cost	Total
40	Remove Existing Sidewalks	330.00 SF	4.00	1,320.00
41	Remove Interior Framed Partitions (By Hand)	253.81 LF	18.00	4,568.58
42	Remove Cabinets & Vanities (By Hand)	22.72 LF	25.00	568.00
43	Remove Plumbing Fixtures (By Hand)	19.00 EA	75.00	1,425.00
44	Remove Doors & Frames (By Hand)	14.00 EA	75.00	1,050.00
45	Remove Appliance (By Hand)	10.00 EA	150.00	1,500.00
46			**Demolition Total**	**$48,108.78**
47	**02.1500 Containers/Waste Removal**			
48	Containers/Waste Removal	1.00 LS	40,000.00	40,000.00
49			**Containers/Waste Removal Total**	**$40,000.00**
50			**Existing Conditions Total**	**$88,108.78**
51	**03 Concrete**			
52	**03.1000 Concrete**			
53	Form & Pour S-2 8" Concrete Planks	617.30 CY	750.00	462,975.00
54	Form & Pour Vertical Concrete Column(s)	533.30 CY	900.00	479,970.00
55	Form & Pour Concrete Planters	2.75 CY	2,500.00	6,875.00
56	Form & Pour Concrete Pad for Generator	1.33 CY	1,000.00	1,330.00
57	Concrete Testing	1.00 LS	15,000.00	15,000.00
58	Form & Pour 8"x12" Grade Beam(s)	128.94 CY	550.00	70,917.00
59	Form & Pour S-1 10" Concrete Slab(s)	118.81 CY	550.00	65,345.50
60	F/I Concrete Stair Pan Infill	222.00 EA	95.00	21,090.00
61	Pump Truck	10.00 EA	1,400.00	14,000.00
62			**Concrete Total**	**$1,137,502.50**
63	**03.3000 Pile Cap Concrete**			
64	F/I Pile Cap-2 [Rectangular 7'x3.5'x3']	15.00 EA	5,104.00	76,560.00
65	F/I Pile Cap-3 [Triangular 5.5'x5.5'x3']	12.00 EA	5,440.00	65,280.00
66			**Pile Cap Concrete Total**	**$141,840.00**
67			**Concrete Total**	**$1,279,342.50**
68	**04 Masonry**			
69	**04.1000 Masonry**			
70	F/I 8" CMU Stem Walls w(1) Filled Cells #5 @ 16" O.C.	10,667.00 BLOCK	26.11	278,526.04
71			**Masonry Total**	**$278,526.04**
72	**04.5710 Terracotta Brick**			
73	F/I Terracotta Brick Cladding	254.13 SF	85.00	21,601.05
74			**Terracotta Brick Total**	**$21,601.05**
75			**Masonry Total**	**$300,127.09**
76	**05 Metal**			
77	**05.0050 Structural Steel**			
78	Fabricate & Erect 2nd Floor Beams	122,511.00 LB	3.70	453,290.70
79	Fabricate & Erect 3rd-5th Floor Beams	235,204.00 LB	3.70	870,254.80
80	Fabricate & Erect Terrace Floor Beams	129,360.00 LB	3.70	478,632.00

Line	Description	Quantity	Unit Cost	Total
81	Fabricate & Erect Steel Columns	28,812.00 LB	3.70	106,604.40
82	Furnish & Install Connection & Base Plates	4,904.00 LB	3.70	18,144.80
83			**Structural Steel Total**	**$1,926,926.70**
84	**05.0100 Misc. Steel**			
85	F/I Railings At Apartment Terraces	196.18 LF	175.00	34,331.50
86	F/I Steel Pan Stairs & Railings	222.00 EA	850.00	188,700.00
87			**Misc. Steel Total**	**$223,031.50**
88			**Metal Total**	**$2,149,958.20**
89	**06 Wood , Plastic and Composites**			
90	**06.2000 Finish Carpentry**			
91	F/I Shade Pockets for Bug Screens	350.00 LF	95.00	33,250.00
92	I/O Interior Wood Door & Casing	16.00 EA	1,000.00	16,000.00
93	I/O Pocket Door	4.00 EA	1,200.00	4,800.00
94	F/I 5/4" Window Stools	8.00 LF	6.50	52.00
95	F/I Base Molding	1,535.60 LF	10.00	15,356.00
96	F/I Door Casing	680.00 LF	10.00	6,800.00
97			**Finish Carpentry Total**	**$76,258.00**
98	**06.2200 Millwork**			
99	F/I Wardrobe Closets	106.60 LF	950.00	101,270.00
100	F/I Millwork Bench & Upholstery @ Living Rooms	36.42 LF	700.00	25,494.00
101	F/I Millwork Bench & Upholstery @ Master Bedrooms	37.56 LF	700.00	26,292.00
102	F/I Laundry Closet Interiors	12.20 LF	200.00	2,440.00
103	F/I VW01 1" Wood Wall Panels @ 2nd - 5th Floors	1,318.41 SF	60.00	79,104.60
104	F/I VW02 2" Wall Panels @ 2nd - 5th Floors	319.23 SF	60.00	19,153.80
105	F/I Upper Cabinets @ Kitchens	41.12 LF	800.00	32,896.00
106	F/I Lower Cabinets @ Kitchens	41.76 LF	1,100.00	45,936.00
107	F/I Kitchen Islands	40.48 LF	1,500.00	60,720.00
108	F/I Double Vanities	38.84 LF	600.00	23,304.00
109	F/I Single Vanities	9.84 LF	600.00	5,904.00
110			**Millwork Total**	**$422,514.40**
111	**06.6600 Decking**			
112	F/I Wood Framed Substrate	1,401.21 SF	22.00	30,826.62
113	F/I IPE Decking w/Drainage & Flashing	1,401.21 SF	35.00	49,042.35
114			**Decking Total**	**$79,868.97**
115			**Wood , Plastic and Composites Total**	**$578,641.37**
116	**07 Thermal and Moisture Protection**			
117	**07.2400 Exterior Insulation & Finish Systems (EIFS)**			
118	F/I VS01 3/4" Stucco @ 1st Floor	5,270.28 SF	20.00	105,405.60
119	F/I VS01 3/4" Stucco @ 2nd - 5th Floors	3,451.66 SF	20.00	69,033.20
120	F/I VS01 3/4" Stucco @ 6th Floor Terrace	3,165.11 SF	20.00	63,302.20
121			**Exterior Insulation & Finish Systems (EIFS) Total**	**$237,741.00**

Line	Description	Quantity	Unit Cost	Total
122	**07.3000 Roofing**			
123	HVHZ Permit Fees, Field Uplift Testing & Waterproofing Tests	1.00 LS	5,000.00	5,000.00
124	F/I Slip Sheet or Protection Mat	1,401.21 SF	2.50	3,503.03
125	Stone Coping Allowance	1.00 LS	30,000.00	30,000.00
126	F/I 1-Ply TPO Roof Membrane with Tapered Polyiso Insulation	2,205.13 SF	18.50	40,794.91
127	F/I 1-Ply TPO Roof Membrane at Parapet Walls	447.51 SF	14.00	6,265.14
128	Flash Roof Drain (Provided by Plumber)	4.00 EA	950.00	3,800.00
129	Flash Overflow Drain (Provided by Plumber)	8.00 EA	700.00	5,600.00
130	Flash Roof Drain (Provided by Plumber)	12.00 EA	700.00	8,400.00
131	Flash Condenser Units	9.00 EA	1,100.00	9,900.00
132			**Roofing Total**	**$113,263.08**
133	**07.9510 Siding**			
134	Dark Wood Effect Porcelain Stoneware For Cladding	618.64 SF	55.00	34,025.20
135			**Siding Total**	**$34,025.20**
136			**Thermal and Moisture Protection Total**	**$385,029.28**
137	**08 Openings**			
138	**08.1100 Doors, Frames & HW**			
139	F/I HM Frame (Single)	7.00 EA	365.00	2,555.00
140	F/O HM Door	7.00 EA	400.00	2,800.00
141	F/O Door Hardware (Commercial Interior)	7.00 EA	500.00	3,500.00
142			**Doors, Frames & HW Total**	**$8,855.00**
143	**08.1400 Wood Doors & HW**			
144	F/O Solid-Core Wood Door	16.00 EA	2,800.00	44,800.00
145	F/O Pocket Door with Kit	4.00 EA	2,500.00	10,000.00
146	F/O Door Hardware	20.00 EA	500.00	10,000.00
147			**Wood Doors & HW Total**	**$64,800.00**
148	**08.4513 Motorized Bug Screens**			
149	F/I Motorized Bug Screens @ 2nd-5th Floors	349.98 LF	370.00	129,492.60
150			**Motorized Bug Screens Total**	**$129,492.60**
151	**08.5000 Windows**			
152	F/O 2'6"x5'0" Aluminum Window w/o Mutins	1.00 EA	1,050.00	1,050.00
153	F/O 5'6"x5'0" Aluminum Window w/o Mutins	1.00 EA	1,600.00	1,600.00
154			**Windows Total**	**$2,650.00**
155	**08.8200 Arch. Metal & Glass**			
156	F/I Curtain Wall Operable Doors	1,214.03 SF	220.00	267,086.60
157	F/I Curtain Wall System	3,689.52 SF	125.00	461,190.00
158	F/I Glass Door & HW @ Baths	4.00 EA	2,600.00	10,400.00
159			**Arch. Metal & Glass Total**	**$738,676.60**
160	**08.8400 Glass Railings**			
161	F/I Glass Railings @ Roof Terrace (Assumed)	61.72 LF	600.00	37,032.00
162			**Glass Railings Total**	**$37,032.00**

Line	Description	Quantity	Unit Cost	Total
163	**08.8500 Shower Enclosures**			
164	F/I Shower Enclosure @ Baths	4.00 EA	3,200.00	12,800.00
165	F/I Master Shower Enclosure (Steam Showers)	4.00 EA	13,500.00	54,000.00
166			**Shower Enclosures Total**	**$66,800.00**
167			**Openings Total**	**$1,048,306.20**
168	**09 Finishes**			
169	**09.2300 Drywall & Carpentry**			
170	Provide Temporary Support @ Existing Structure Post Demolition	1.00 LS	1,500.00	1,500.00
171	F/I 54"x30" Access Panel(s)	9.00 EA	250.00	2,250.00
172	I/O Windows @ Commercial Office	2.00 EA	250.00	500.00
173	F/I 5/8" GWB Walls (Level 5 Finish)	14,880.15 SF	4.50	66,960.70
174	F/I CP01 5/8" GWB Ceilings @ 1st Floor (Level 5 Finish)	1,312.86 SF	4.50	5,907.87
175	F/I CP01 5/8" GWB Ceilings @ 2nd-5th Floors (Level 5 Finish)	8,134.08 SF	4.50	36,603.36
176	F/I CP01 5/8" GWB Ceilings @ 6th Floor (Level 5 Finish)	352.27 SF	4.50	1,585.22
177	F/I 5/8" Durock	320.64 SF	2.00	641.28
178	F/I Blanket Insulation	11,060.96 SF	1.50	16,591.46
179	I/O Bath Accessories	16.00 BATH	500.00	8,000.00
180	I/O Interior Door, Frame & HW	7.00 EA	225.00	1,575.00
181	F/I 1-5/8" Metal Stud Framing	16,079.85 SF	4.00	64,319.40
182	F/I 2-1/2" Metal Stud Framing	1,188.78 SF	4.50	5,349.51
183	F/I 3-5/8" Metal Stud Framing	1,718.91 SF	5.50	9,454.01
184	F/I 6" Metal Stud Framing	1,872.63 SF	6.25	11,703.94
185	F/I 5/8" Plywood Walls @ 2nd Through 5th Floor	912.76 SF	4.60	4,198.70
186			**Drywall & Carpentry Total**	**$237,140.45**
187	**09.3013 Tile & Stone**			
188	F/I FT-01 Floor Tile @ 1st Floor	583.81 SF	45.50	26,563.33
189	F/I FT-02 Floor Tile @ 2nd Floor	469.88 SF	45.50	21,379.59
190	F/I FT-01 Floor Tile @ 2nd-5th Floors	6,532.23 SF	45.50	297,216.39
191	F/I FT-02 Floor Tile @ 2nd-5th Floors	1,430.40 SF	45.50	65,083.20
192	F/I FT-01 Floor Tile @ Terrace	60.10 SF	45.50	2,734.55
193	F/I Unspecified Floor Tile @ Terrace	89.15 SF	45.50	4,056.45
194	F/I Floor Tile @ Steam Shower Ceilings	73.07 SF	47.50	3,470.90
195	F/I Mud Job at Shower	8.00 EA	500.00	4,000.00
196	F/I Waterproofing for Floor Tile	73.07 SF	5.25	383.62
197			**Tile & Stone Total**	**$424,888.03**
198	**09.9100 Painting**			
199	Paint GWB Walls	10,909.80 SF	1.30	14,182.74
200	Paint Base Molding	1,535.60 LF	3.50	5,374.60
201	Paint GWB Ceilings	9,799.21 SF	1.30	12,738.97
202	Paint/Stain New Doors & Casing	20.00 EA	225.00	4,500.00
203	Paint HM Door & Frame	7.00 EA	150.00	1,050.00

Line	Description	Quantity	Unit Cost	Total
204			**Painting Total**	**$37,846.31**
205			**Finishes Total**	**$699,874.79**
206	**10 Specialties**			
207	**10.2800 Bath Accessories**			
208	Bath Accessories Budget (High-End Residential Master Bath)	8.00 EA	3,000.00	24,000.00
209	Bath Accessories Budget (High-End Residential Guest Bath/Powder Room)	8.00 EA	1,500.00	12,000.00
210			**Bath Accessories Total**	**$36,000.00**
211			**Specialties Total**	**$36,000.00**
212	**11 Equipment**			
213	**11.3100 Appliances**			
214	F/O Electric Wall Oven	4.00 EA	7,000.00	28,000.00
215	F/O Stacking Kits	4.00 EA	200.00	800.00
216	Delivery, Install & Warranty	1.00 LS	12,000.00	12,000.00
217	F/O Washer	4.00 EA	2,500.00	10,000.00
218	F/O Electric Dryer	4.00 EA	2,500.00	10,000.00
219	F/O Refrigerator	4.00 EA	12,500.00	50,000.00
220	F/O Dishwasher	4.00 EA	3,500.00	14,000.00
221	F/O Electric Cooktop	4.00 EA	5,000.00	20,000.00
222	F/O Freezer	4.00 EA	8,000.00	32,000.00
223			**Appliances Total**	**$176,800.00**
224	**11.3200 Outdoor Kitchen**			
225	F/I Outdoor BBQ Cabinets & Countertops	13.68 LF	2,800.00	38,304.00
226			**Outdoor Kitchen Total**	**$38,304.00**
227	**11.8200 Trash Compactor**			
228	F/I Trash Compactor (Per Floor)	5.00 EA	7,800.00	39,000.00
229			**Trash Compactor Total**	**$39,000.00**
230			**Equipment Total**	**$254,104.00**
231	**12 Furnishing**			
232	**12.3600 Countertops**			
233	Fabricate, Template & Install Stone Countertops @ Double Vanities	77.68 SF	155.00	12,040.40
234	Fabricate, Template & Install Stone Countertops @ Single Vanities	19.68 SF	155.00	3,050.40
235	Fabricate, Template & Install Stone Countertops @ Kitchens	212.27 SF	155.00	32,901.85
236	Fabricate, Template & Install Stone Bench @ Master Showers	37.36 SF	180.00	6,724.80
237	Fabricate, Template & Install Stone Backsplash @ 2nd - 5th Floors	126.00 SF	155.00	19,530.00
238	Fabricate, Template & Install 1-1/4" Stone At Walls @ 2nd - 5th Floors	929.00 SF	155.00	143,995.00
239	Fabricate, Template & Install Stone Waterfall Edges @ Kitchens	72.84 SF	155.00	11,290.20
240			**Countertops Total**	**$229,532.65**
241			**Furnishing Total**	**$229,532.65**
242	**14 Conveying System**			
243	**14.2000 Elevator**			

Line	Description	Quantity	Unit Cost	Total
244	F/I Machine Room-Less (MRL) Traction Elevator	6.00 EA	35,000.00	210,000.00
245			**Elevator Total**	**$210,000.00**
246			**Conveying System Total**	**$210,000.00**
247	**21 Fire Suppression**			
248	**21.0000 Sprinkler**			
249	Excavation & Backfill for Underground Service	111.00 LF	115.00	12,765.00
250	F/I 4"x2-1/2"x2-1/2" Fire Department Connection	1.00 EA	3,000.00	3,000.00
251	F/I Fire Pump	1.00 EA	14,000.00	14,000.00
252	F/I 4" DDCV	1.00 EA	1,800.00	1,800.00
253	F/I Domestic Water Pump	1.00 EA	7,000.00	7,000.00
254	F/I 2" Piping	497.04 LF	12.00	5,964.48
255	F/I 1" Piping	225.30 LF	8.00	1,802.40
256	F/I 4" Piping	429.24 LF	20.00	8,584.80
257	F/I Flow Switch	9.00 EA	250.00	2,250.00
258	F/I Automatic Wet Standpipe	9.00 EA	3,500.00	31,500.00
259	F/I Fire Hose Cabinet	1.00 EA	1,200.00	1,200.00
260	F/I 2-1/2" Piping	169.00 LF	15.00	2,535.00
261	F/I Fire Cabinet Hose	8.00 EA	400.00	3,200.00
262	F/I 4'x2-1/2"x2-1/2" Roof Manifold (250 GPM 100 PSI)	2.00 EA	3,800.00	7,600.00
263	Extend 4" Pipe to Existing Fire Hydrant on Meridian CT	110.79 LF	55.00	6,093.45
264	F/I 6" Ductile Iron Pipe	111.00 LF	90.00	9,990.00
265	Connect to Existing Hydrant	1.00 EA	2,000.00	2,000.00
266	Road Opening Permit & Traffic Control	1.00 LS	6,000.00	6,000.00
267	New Sprinkler Heads	80.00 EA	375.00	30,000.00
268	Sprinkler Permits, Filing, Inspections, Signoff & Hydrostatic Testing	1.00 LS	5,000.00	5,000.00
269			**Sprinkler Total**	**$162,285.13**
270			**Fire Suppression Total**	**$162,285.13**
271	**22 Plumbing**			
272	**22.0000 Plumbing**			
273	F/I 1-1/2" S.O.V. Water Line	141.95 LF	35.00	4,968.25
274	F/I 1" Backflow Preventer	1.00 EA	1,050.00	1,050.00
275	F/I 1-1/2" Backflow Preventer	1.00 EA	1,750.00	1,750.00
276	F/I 1" S.O.V. Water Line	58.86 LF	32.00	1,883.52
277	F/I 3/4" Water Line	9.39 LF	30.00	281.70
278	F/I Domestic Pump AMT Heavy Duty Straight Centrifugal Pumps Model 4240 Series 2"x1.5. HP	1.00 EA	6,000.00	6,000.00
279	F/I 3/4" Hot Water Piping	388.81 LF	35.00	13,608.35
280	F/I 3/4" Cold Water Piping	481.57 LF	35.00	16,854.95
281	F/I 4" Drainage Piping	107.95 LF	65.00	7,016.75
282	F/I 3" Drainage Piping	221.00 LF	55.00	12,155.00
283	F/I 4" Overflow Drainage Piping	83.21 LF	65.00	5,408.65

Line	Description	Quantity	Unit Cost	Total
284	F/I 3" Vertical Drainage Piping	180.00 LF	65.00	11,700.00
285	F/I 4" Vertical Drainage Piping	120.00 LF	70.00	8,400.00
286	F/I 2" Sanitary Piping @ 2nd-5th Floors	213.32 LF	50.00	10,666.00
287	F/I 3" Sanitary Piping @ 2nd-5th Floors	58.12 LF	55.00	3,196.60
288	F/I 2" VTR	350.00 LF	45.00	15,750.00
289	F/I 2" Vent Piping	17.88 LF	45.00	804.60
290	F/I 2" Drainage Piping	24.98 LF	45.00	1,124.10
291	F/I Instant Hot Water Heaters @ Master Showers	4.00 EA	2,000.00	8,000.00
292	F/I Steam Units	4.00 EA	6,500.00	26,000.00
293	F/I Instant Hot Water Heaters @ Bathrooms	8.00 EA	2,000.00	16,000.00
294	Disconnect Existing Plumbing Fixtures	19.00 EA	150.00	2,850.00
295	I/O Residential Toilet	1.00 EA	1,200.00	1,200.00
296	I/O Residential Toilet @ Master Bathrooms	4.00 EA	1,200.00	4,800.00
297	I/O Residential Toilets	4.00 EA	500.00	2,000.00
298	I/O Residential Toilets @ Powder Rooms	4.00 EA	500.00	2,000.00
299	I/O Residential Toilet	1.00 EA	500.00	500.00
300	I/O Bath Lav (Sink) & Faucet	13.00 EA	1,100.00	14,300.00
301	I/O Bath Lav (Sink) & Faucet	4.00 EA	600.00	2,400.00
302	I/O Showers	4.00 EA	1,800.00	7,200.00
303	I/O Custom Shower @ Master Baths	4.00 EA	3,600.00	14,400.00
304	I/O Sink & Faucet	4.00 EA	1,200.00	4,800.00
305	I/O Sink & Faucet	4.00 EA	600.00	2,400.00
306	I/O Appliance	8.00 EA	700.00	5,600.00
307	I/O Dishwasher	11.00 EA	800.00	8,800.00
308	I/O Dishwasher	1.00 EA	500.00	500.00
309	F/I Freezer Waterline	4.00 EA	260.00	1,040.00
310	F/I Refrigerator Waterline	4.00 EA	260.00	1,040.00
311	F/I Gas Piping & Connection for Range	4.00 EA	900.00	3,600.00
312	F/I Instant Hot Water Heater @ Commercial Office	1.00 EA	3,200.00	3,200.00
313	F/I 2" Sanitary Line	5.90 LF	50.00	295.00
314	F/I 3" Sanitary Line	99.97 LF	55.00	5,498.35
315	F/I 4" Sanitary Line	95.31 LF	65.00	6,195.15
316	F/I 5" Sanitary Line	37.45 LF	75.00	2,808.75
317	F/I Roof Drain	4.00 EA	750.00	3,000.00
318	F/I Roof Drain	20.00 EA	850.00	17,000.00
319	F/I Pipe For Roof Drain (Vertical Runs)	200.00 LF	55.00	11,000.00
320	F/I Pipe For Roof Drains (Horizontal Runs)	83.03 LF	55.00	4,566.65
321	Disconnect Existing Appliances	10.00 EA	150.00	1,500.00
322			**Plumbing Total**	**$307,112.37**
323	**22.4000 Plumbing Fixtures**			
324	F/O Kitchen Sinks	8.00 EA	1,500.00	12,000.00

Line	Description	Quantity	Unit Cost	Total
325	F/O Kitchen Faucets	8.00 EA	1,600.00	12,800.00
326	F/O Lav Sinks @ Commercial Office	1.00 EA	1,000.00	1,000.00
327	F/O Lav Sinks @ Master Baths	8.00 EA	1,600.00	12,800.00
328	F/O LAV Sinks	4.00 EA	1,200.00	4,800.00
329	F/O LAV Sinks @ Powder Rooms	3.00 EA	1,200.00	3,600.00
330	F/O LAV Sinks @ Terrace Bath	1.00 EA	1,200.00	1,200.00
331	F/O Lav Faucets @ Commercial Office	1.00 EA	600.00	600.00
332	F/O Lav Faucets @ Master Baths	8.00 EA	1,500.00	12,000.00
333	F/O Lav Faucets	4.00 EA	1,200.00	4,800.00
334	F/O Lav Faucets @ Powder Rooms	3.00 EA	1,000.00	3,000.00
335	F/O Lav Faucets @ Terrace Bath	1.00 EA	1,200.00	1,200.00
336	F/O Residential Toilet @ Commercial Office	1.00 EA	650.00	650.00
337	F/O Residential Toilets @ Master Baths	4.00 EA	8,000.00	32,000.00
338	F/O Residential Toilets	4.00 EA	1,000.00	4,000.00
339	F/O Residential Toilets @ Powder Rooms	4.00 EA	2,000.00	8,000.00
340	F/O Residential Toilets @ Terrace Bath	1.00 EA	2,000.00	2,000.00
341	F/O Custom Shower Kits	4.00 EA	2,500.00	10,000.00
342	F/O Custom Shower Kits @ Master Baths	4.00 EA	2,500.00	10,000.00
343			**Plumbing Fixtures Total**	**$136,450.00**
344			**Plumbing Total**	**$443,562.37**
345	**23 Heating, Ventilating and Air-Conditioning**			
346	**23.0000 HVAC**			
347	Shop Drawings, Balancing Report & As-Builds	1.00 LS	8,500.00	8,500.00
348	F/I FC-4 LHN488HB	1.00 EA	2,000.00	2,000.00
349	F/I CU-4 LUU480HHV	1.00 EA	3,800.00	3,800.00
350	F/I CAS-1 [265 CFM LMCN078HV]	1.00 EA	125.00	125.00
351	F/I 8" Flex Ductwork	79.90 LF	12.00	958.80
352	F/I 10" Flex Ductwork	29.39 LF	13.00	382.07
353	F/I RAG 36"x3"	10.00 EA	95.00	950.00
354	F/I RAG 24"x4"	3.00 EA	75.00	225.00
355	F/I 16"x3" 600 CFM Diffuser	1.00 EA	300.00	300.00
356	F/I 24"x3" 200 CFM Diffuser	25.00 EA	150.00	3,750.00
357	F/I 18"x3" 150 CFM Diffuser	1.00 EA	120.00	120.00
358	F/I RAG 76"x4" Diffuser	1.00 EA	350.00	350.00
359	F/I 30"X3" 300 CFM Diffuser(S)	10.00 EA	200.00	2,000.00
360	F/I 42"x32" Access Panel	4.00 EA	300.00	1,200.00
361	F/I RAG 36"x18"	4.00 EA	125.00	500.00
362	F/I Louvers - Color Sample Champagne Gold	2,654.77 SF	10.00	26,547.70
363	F/I F.C.-3.1 LHN368HV 3-Ton	4.00 EA	6,790.00	27,160.00
364	F/I F.C.-1.1 LHN368HV 3-Ton	4.00 EA	6,790.00	27,160.00
365	F/I 6" Wall Cap	15.00 EA	270.00	4,050.00

Line	Description	Quantity	Unit Cost	Total
366	F/I 4" Vent Piping from 2nd Floor to Roof (3 Bathrooms)	120.00 LF	30.00	3,600.00
367	F/I 4" Horizontal Vent Piping	86.86 LF	30.00	2,605.80
368	F/I RAG 48"x3" Grill	8.00 EA	80.00	640.00
369	F/I CAS-2 265 CFM LMN078HV	4.00 EA	120.00	480.00
370	F/I 12"x2" 50 CFM	4.00 EA	50.00	200.00
371	F/I 6" Flex Ductwork	56.93 LF	4.00	227.72
372	F/I 50"x3" Diffuser 450 CFM	4.00 EA	150.00	600.00
373	F/I RAG 26"x18"	4.00 EA	250.00	1,000.00
374	F/I 12"x12" 50 CFM	4.00 EA	75.00	300.00
375	Provide Low-Voltage Wiring to HVAC Units	9,996.00 SF	1.25	12,495.00
376	F/I 4" Exhaust Piping from 1st Floor to Roof EF#1	50.00 LF	40.00	2,000.00
377	F/I 14"x10" Ductwork	32.29 LB	18.50	597.37
378	F/I 30"x10" Ductwork	44.18 LB	18.50	817.33
379	F/I 40"x10" Ductwork	61.53 LB	18.50	1,138.31
380	F/I 20"x10" Ductwork	59.06 LB	18.50	1,092.61
381	F/I 22"x8" Ductwork	1,220.79 LB	18.00	21,974.22
382	F/I 30"x8" Ductwork	2,602.92 LB	18.00	46,852.56
383	F/I 24"x8" Ductwork	812.97 LB	18.00	14,633.46
384	F/I 18"x8" Ductwork	453.85 LB	18.00	8,169.30
385	F/I Refrigerant Piping	249.08 LF	30.00	7,472.40
386	F/I Refrigerant Piping @ Roof	1,800.00 LF	30.00	54,000.00
387	F/I Condensate Piping	91.54 LF	35.00	3,203.90
388			**HVAC Total**	**$294,178.55**
389			**Heating, Ventilating and Air-Conditioning Total**	**$294,178.55**
390	**26 Electrical**			
391	**26.0000 Electric**			
392	F/I Elevator Power Supply, Wiring, Breakers, etc.	1.00 LS	11,500.00	11,500.00
393	F/I Generator [Generac Industrial Diesel Generator SD150 6.7L 150KW 134 GAL Weather Protected Enclosure]	1.00 LS	68,000.00	68,000.00
394	F/I Cafe Panel CF 100Amp	1.00 EA	3,650.00	3,650.00
395	Wire Water Pump	1.00 EA	620.00	620.00
396	Wire Jockey Pump	1.00 EA	750.00	750.00
397	Wire Fire Pump	1.00 EA	1,650.00	1,650.00
398	Wire Fire Pump Controller	1.00 EA	560.00	560.00
399	F/I Disconnect Switch	7.00 EA	875.00	6,125.00
400	F/I Disconnect Switch @ 1st - 5th Floors	13.00 EA	875.00	11,375.00
401	Wire Cassette Unit @ 1st - 5th Floors	4.00 EA	690.00	2,760.00
402	Provide Temporary Lighting & Power	9,996.00 SF	2.00	19,992.00
403	F/I Home Run + Arc-Fault Breaker	48.00 EA	275.00	13,200.00
404	F/I Duplex Receptacle	97.00 EA	105.00	10,185.00
405	F/I GFI Receptacle @ 1st - 5th Floors	52.00 EA	105.00	5,460.00

Line	Description	Quantity	Unit Cost	Total
406	F/I Weatherproof GFI Receptacle @ 6th Floor Terrace	3.00 EA	220.00	660.00
407	F/I Weatherproof GFI Receptacle	4.00 EA	220.00	880.00
408	F/I GFI Receptacle @ 1st Floor	10.00 EA	250.00	2,500.00
409	240V Receptacle @ 1st - 5th Floors	12.00 EA	340.00	4,080.00
410	Wire 20 Amp HWH @ 1st - 5th Floor	8.00 EA	410.00	3,280.00
411	Wire 60 Amp AC Condenser Unit @ 6th Floor Terrace	10.00 EA	1,300.00	13,000.00
412	Wire Cassette Units @ 6th Floor Terrace	2.00 EA	690.00	1,380.00
413	I/O Lighting Fixtures	51.00 EA	175.00	8,925.00
414	I/O Install Exit Sign	19.00 EA	175.00	3,325.00
415	I/O Lighting Fixtures	396.00 EA	175.00	69,300.00
416	F/I Ceiling Junction Box for Bathroom Exhaust Fan @ 1st - 5th Floor	8.00 EA	100.00	800.00
417	F/I Junction Box For Kitchen Exhaust @ 1st - 5th Floors	5.00 EA	170.00	850.00
418	F/I Junction Box Bathroom Exhaust Fan @ 6th Floor Terrace	1.00 EA	170.00	170.00
419	F/I Single-Pole Switch @ 1st - 5th Floors	44.00 EA	95.00	4,180.00
420	SF/I ingle-Pole Switch @ 6th Floor Terrace	11.00 EA	95.00	1,045.00
421	F/I Single-Pole Switch @ 1st Floor OP? Is This Occupancy Sensor	12.00 EA	140.00	1,680.00
422	F/I 3-Way Switch @ 1st Floor	8.00 EA	140.00	1,120.00
423	F/I 3-Way Switch @ 1st - 5th Floors	57.00 EA	140.00	7,980.00
424	Electrical Disconnects Prior to Demo	1.00 EA	850.00	850.00
425	F/I Floor Mounted Junction Box For Floor Outlet @ 1st Floor	5.00 EA	275.00	1,375.00
426	F/I Panel A 250Amp	1.00 EA	6,500.00	6,500.00
427	F/I Panel B 200Amp	1.00 EA	5,250.00	5,250.00
428	F/I Panel C 150Amp	1.00 EA	4,400.00	4,400.00
429	F/I Panel D 150Amp	1.00 EA	4,400.00	4,400.00
430	F/I HH-1 400 Amp Panel	1.00 EA	7,500.00	7,500.00
431	F/I 3" Conduit for Underground Electrical Service	100.00 LF	18.00	1,800.00
432	F/I Feeder Wire (3) #600 KCM Copper Feeder	100.00 LF	15.00	1,500.00
433	Underground Electrical Service Inspection	1.00 EA	500.00	500.00
434	F/O Terminations and Connections for 400 Amp Service	1.00 EA	2,500.00	2,500.00
435			**Electric Total**	**$317,557.00**
436	**26.5000 Lighting Fixtures**			
437	F/I Lighting Fixtures	447.00 EA	350.00	156,450.00
438	Emergency (EM) Lighting Fixture @ 1st Floor	5.00 EA	450.00	2,250.00
439	Emergency (EM) Lighting Fixture @ 1st - 5th Floor	28.00 EA	450.00	12,600.00
440	Emergency (EM) Lighting Fixture @ 6th Floor Terrace	3.00 EA	450.00	1,350.00
441	Exit Sign	19.00 EA	160.00	3,040.00
442			**Lighting Fixtures Total**	**$175,690.00**
443			**Electrical Total**	**$493,247.00**
444	**27 Communications**			
445	**27.1020 Audio Visual**			
446	F/I Speakers	3.00 EA	240.00	720.00

Line	Description	Quantity	Unit Cost	Total
447	F/I Speakers @ 1st Floor	3.00 EA	240.00	720.00
448	F/I Speakers @ 2nd - 5th Floors	23.00 EA	240.00	5,520.00
449	F/I Speakers @ 6th Floor Terrace	1.00 EA	240.00	240.00
450			**Audio Visual Total**	**$7,200.00**
451			**Communications Total**	**$7,200.00**
452	**28 Safety And Security**			
453	**28.4600 Fire Alarm**			
454	F/I Elevatator FA Connections	1.00 LS	3,000.00	3,000.00
455	Heat Detector @ 1st Floor	1.00 EA	150.00	150.00
456	Smoke/Carbon Monoxide Detector Combo @ 1st Floor	3.00 EA	200.00	600.00
457	Smoke/Carbon Monoxide Detector Combo @ 1st - 5th Floor	32.00 EA	200.00	6,400.00
458	Fire Alarm Programming	1.00 EA	2,500.00	2,500.00
459	Pull Station @ 1st Floor	1.00 EA	300.00	300.00
460	Addressable Manual Station @ 1st - 5th Floor	8.00 EA	300.00	2,400.00
461	Addressable Manual Station @ 6th Floor Terrace	3.00 EA	300.00	900.00
462	Horn/Strobe @ 1st Floor	3.00 EA	350.00	1,050.00
463	Horn/Strobe @ 1st - 5th Floor	8.00 EA	350.00	2,800.00
464	Low Frequency Horn @ 1st - 5th Floor	8.00 EA	350.00	2,800.00
465	Horn/Strobe @ 6th Floor Terrace	3.00 EA	350.00	1,050.00
466			**Fire Alarm Total**	**$23,950.00**
467	**28.4610 Security**			
468	F/I Surveillance Cameras TR01, TR02 @1st Floor	10.00 EA	480.00	4,800.00
469	F/I TR02 Cameras @ 6th Floor Terrace	5.00 EA	480.00	2,400.00
470			**Security Total**	**$7,200.00**
471			**Safety And Security Total**	**$31,150.00**
472	**31 Sitework**			
473	**31.0000 Sitework**			
474	Post-Demolition Grading	1.00 DAY	2,500.00	2,500.00
475	Reconstruct Swale/Sod Along Entire Property	1,800.00 SF	2.65	4,770.00
476	Export Fill	18.52 CY	80.00	1,481.60
477	Import Fill	6.77 CY	160.00	1,083.20
478	Trenching, Sand & Backfill for Water & Waste	250.00 LF	18.00	4,500.00
479	Excavate Foundation (Slab on Grade)	1.58 DAY	2,600.00	4,108.00
480	Excavate Foundation (Frost Walls)	6.48 DAY	2,500.00	16,200.00
481	Backfill Slab & Compact	1.98 DAY	2,600.00	5,148.00
482	F/I 6" Lime Rock Base	66.00 CY	60.00	3,960.00
483	Trenching, Sand and Backfill Utility Trench for Underground Electric (2' Deep w/1' Sand)	100.00 LF	16.00	1,600.00
484			**Sitework Total**	**$45,350.80**
485	**31.1100 Drainage & Stormwater**			
486	F/I Nyoplast Drain Basins & All Associated Piping	4.00 EA	5,200.00	20,800.00

Line	Description	Quantity	Unit Cost	Total
487	F/I Slot Drains & All Associated Piping	3.00 EA	2,400.00	7,200.00
488	F/I Trench Drain [Zurn Z-112]	56.24 LF	120.00	6,748.80
489	Additional Stabilization Required For Sandy Soil	1.00 LS	1,500.00	1,500.00
490	F/I Wash Rock	21.13 CY	60.00	1,267.80
491	F/I 4" HDPE Pipe for Planter	20.00 LF	5.00	100.00
492	F/I 15" HDPE Pipe	101.40 LF	40.00	4,056.00
493	F/I Trench Drain [Zurn Z-884]	4.67 LF	200.00	934.00
494			**Drainage & Stormwater Total**	**$42,606.60**
495	**31.2500 Erosion And Sedimentation Controls**			
496	Protect Existing Trees	3.00 EA	250.00	750.00
497	F/I 6' Temporary Double Swing Gate w/Canvas	1.00 EA	950.00	950.00
498	F/I Gravel at Temporary Construction Entrance	106.23 SF	4.00	424.92
499	F/I Siltsack Material to Drain Basin to Prevent Silt Entering	5.00 EA	200.00	1,000.00
500	Inspection and Maintenance of BMPs	6.00 EA	200.00	1,200.00
501	F/I Silt Fence	300.62 LF	6.00	1,803.72
502	F/I Construction Entrance (Steel Plates + Gravel)	1.00 EA	4,800.00	4,800.00
503			**Erosion And Sedimentation Controls Total**	**$10,928.64**
504	**31.3116 Termite Control**			
505	Termite Control Application, Certification & Signage	1.00 EA	1,800.00	1,800.00
506			**Termite Control Total**	**$1,800.00**
507	**31.6323 Auger Cast Grout Piles**			
508	F/I P-3 3.5" Helix Piles	24.00 EA	1,800.00	43,200.00
509	F/I P-2 14" Auger Cast Pile(s)	21.00 EA	3,200.00	67,200.00
510	F/I P-1 Auger Cast Piles	77.00 EA	2,000.00	154,000.00
511			**Auger Cast Grout Piles Total**	**$264,400.00**
512			**Sitework Total**	**$365,086.04**
513	**32 Exterior Improvements**			
514	**32.1200 Paving**			
515	Striping	1.00 LS	725.00	725.00
516	Resurface Driveway (Type S-III Asphalt)	1,130.00 SF	4.50	5,085.00
517	Restore Existing Main Roads	666.00 SF	11.00	7,326.00
518	Mill 2" of Existing Asphalt Paving	1,130.00 SF	2.50	2,825.00
519			**Paving Total**	**$15,961.00**
520	**32.1600 Site Concrete**			
521	Form & Pour Sidewalks	330.00 SF	12.00	3,960.00
522			**Site Concrete Total**	**$3,960.00**
523	**32.1900 Misc. Site Furnishings**			
524	F/I Concrete Wheel Stop	5.00 EA	325.00	1,625.00
525			**Misc. Site Furnishings Total**	**$1,625.00**
526	**32.3200 Retaining Wall**			
527	F/I Concrete Retaining Wall	575.76 SF	45.00	25,909.20

Line	Description	Quantity	Unit Cost	Total
528			**Retaining Wall Total**	**$25,909.20**
529	**32.8000 Irrigation**			
530	F/I 2" Irrigation Supply Lines	411.14 LF	5.00	2,055.70
531	F/I Irrigation Backflow Preventer (PVB)	1.00 EA	850.00	850.00
532	F/I Nozzles and Bubblers [RainBird 1800 PRS-U, Strip Nozzles]	31.00 EA	150.00	4,650.00
533	F/I Valves [RainBird PEB Series]	2.00 EA	950.00	1,900.00
534			**Irrigation Total**	**$9,455.70**
535	**32.9300 Landscaping**			
536	F/I SBU Trees	5.00 EA	2,500.00	12,500.00
537	F/I LG Trees	7.00 EA	2,500.00	17,500.00
538	F/I MF Trees	2.00 EA	2,500.00	5,000.00
539	F/I GR Trees	14.00 EA	2,500.00	35,000.00
540	F/I JC Trees	4.00 EA	2,500.00	10,000.00
541	F/I CAG Trees	1.00 EA	2,500.00	2,500.00
542	F/I PP Trees [Pidgeon Plum]	7.00 EA	2,500.00	17,500.00
543	F/I ZZ Trees	7.00 EA	2,500.00	17,500.00
544	F/I DRA Trees	3.00 EA	2,500.00	7,500.00
545	F/I RE Trees	3.00 EA	2,500.00	7,500.00
546	Backfill & Surface Grade Planting(s) w/Topsoil	50.00 EA	35.00	1,750.00
547	F/I SS Bushes	16.00 EA	500.00	8,000.00
548	F/I Mulch	74.32 CY	55.00	4,087.60
549			**Landscaping Total**	**$146,337.60**
550	**32.9620 Site Signage**			
551	Parking/Traffic Signs	1.00 EA	350.00	350.00
552			**Site Signage Total**	**$350.00**
553			**Exterior Improvements Total**	**$203,598.50**
554	**Sub-Total (Base Cost)**			**$10,580,825.45**

Estimate Summary

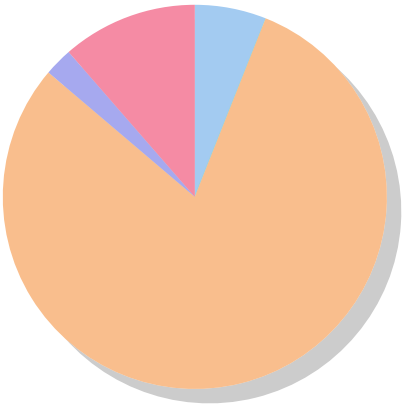

Material [$636,722]
Labor [$0]
SubContractor [$8,485,280]
Equipment [$252,240]
Other [$1,206,583]

Description		Total
Sub-Total (Base Cost)		$10,580,825.45
Material	10.0000%	63,672.23
Sub-Total ()		$10,644,497.68
Fee	5.0000%	532,224.88
Insurance	3.0000%	335,301.68
Total Estimate		$11,512,024.24
